

NB 110 Progress Report

Contents

Virtus XP Renfer	3
Virtus XP Construction Photos	4
Virtus XP Building Schedule	11
Virtus XP Client Decision List	13




































NB113 BUILDING SCHEDULE

		2023																																									
		JUNE			JULY			AUGUST			SEPTEMBER			OCTOBER			NOVEMBER			DECEMBER			JANUARY			FEBRUARY			MARCH			APRIL			MAY								
		1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4		
BUILDING WORKS	1 Steel hull (Include steel outfitting)																																										
	1. Block																																										
	2. Block																																										
	3. Block																																										
	4. Block																																										
	5. Block																																										
	6. Block																																										
	Tanks tests																																										
	Outfitting works after rotation of the hull																																										
	2 Aluminium superstructure (Include aluminium outfitting)																																										
1. Block																																											
2. Block																																											
3. Block																																											
4. Block																																											
Outfitting																																											
3 Sand blasting																																											
4 Furniture																																											
Mascoat, insulation, electrical and piping works of the <u>below deck guest cabins</u>																																											
Furniture works of <u>below deck guest cabins</u>																																											
Mascoat, insulation, electrical and piping works of the <u>below deck crew cabins, crew mess and galley</u>																																											
Furniture works of below deck <u>crew cabins, crew mess and galley</u>																																											
Mascoat, insulation, electrical and piping works of the <u>main deck</u>																																											
Furniture works of <u>main deck VIP cabins</u>																																											
Furniture works of <u>main deck Salon, Pantry and corridor</u>																																											
Mascoat, insulation, electrical and piping works of the <u>Upper deck</u>																																											
Furniture works of <u>master cabin</u>																																											
Furniture works of <u>sky lounge, pantry and corridor</u>																																											
Mascoat, insulation, electrical and piping works of the <u>sun deck</u>																																											
Furniture works of <u>wheelhouse</u>																																											
6 Technical zones equipments installation outfitting																																											
7 Stainless steel																																											
8 Electrical works																																											
9 Piping works																																											
5 Filler and primer works																																											
1.Primer (Interprime 820)																																											
1. Filler (Interfill 830)																																											
2. Filler (Interfill 833)																																											
2.Primer (Interprime 820)																																											
Last coat primer																																											
10 Top coat paint application																																											

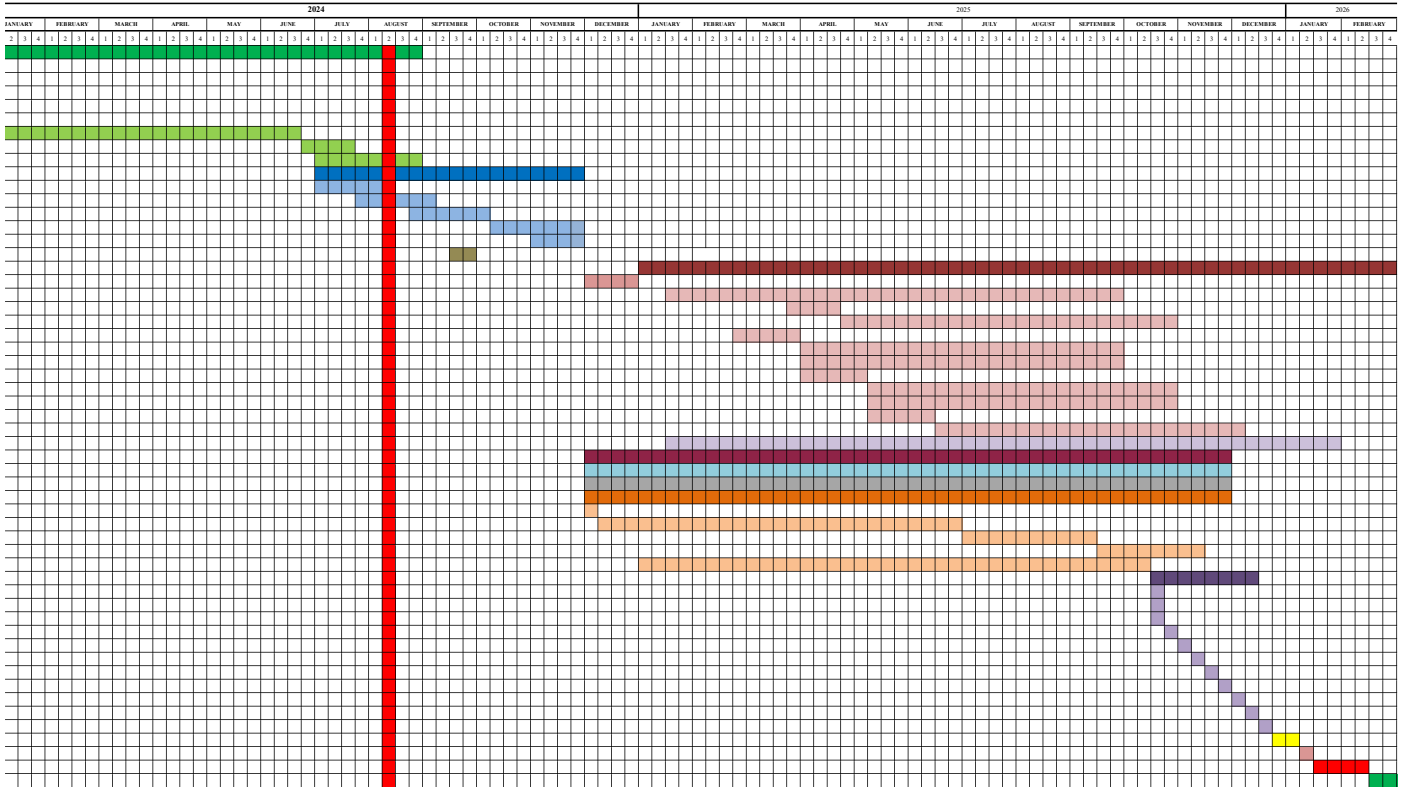

Date of Agreement			Date of Decision
GENERAL		Approval of General Arrangement Plan	30.03.2024
GENEL		Deciding of yacht name and logo	1.01.2025
ELECTRONIC		Selection of the music system (audio & video), TV system, Aoutomation abd Camara System	1.01.2025
GENERAL		Decision of the Client's Representative	TBD
GENERAL		Decision of Port of Registry	1.01.2025
INTERIOR DESIGN	Interior Equipment	Selection of galley equipment	15.06.2024
EXTERIOR DESIGN		Decision of the color of the paint	1.05.2025
ELECTRONIC		Decision of the navigation and communication equipments	1.01.2025
ELECTRONIC		Decision of the internet and satelitte system	1.01.2025
INTERIOR DESIGN	Interior Equipment	Selection of the bathroom accessories	15.10.2024
EXTERIOR DESIGN		Decision of the place of the tents and umbrellas & their design	
GENERAL		Decision of the tender boat	1.01.2025
INTERIOR DESIGN	Lower Deck	Submission of the Lower Deck Interior Design Renders to the Client and getting the client's comments	15.08.2024
INTERIOR DESIGN	Lower Deck	Approval of Lower Deck Interior Design Renders by the Client	15.09.2024
INTERIOR DESIGN	Main Deck	Submission of the Main Deck Interior Design Renders to the Client and getting the client's comments	15.11.2024
INTERIOR DESIGN	Main Deck	Approval of MainDeck Interior Design Renders by the Client	30.11.2024
INTERIOR DESIGN	Upper Deck	Submission of the Upper Deck Interior Design Renders to the Client and getting the client's comments	30.12.2024
INTERIOR DESIGN	Upper Deck	Approval of Upper Deck Interior Design Renders by the Client	15.01.2025
INTERIOR DESIGN	General	Approval of the moodboard by the client	15.10.2024
INTERIOR DESIGN	Sun Deck	Decision of the wheelhouse layout and approval of the design	1.02.2025
INTERIOR DESIGN	Interior Equipment	Decision of the interior loose furniture	30.01.2026
EXTERIOR DESIGN		Decision of layout of the exterior areas and revisions	30.12.2025
EXTERIOR DESIGN		Decision of the exterior loos furniyure and fabric	30.01.2026
INTERIOR DESIGN	Interior Equipment	Decision of the decorative accessories	30.03.2026
INTERIOR DESIGN	Interior Equipment	Delivery of the dishare, glassware, linens, sheets etc to the shipyard	30.05.2026

NOTE : Above mentioned dates are subject to change by the shipyard according to the contrustion stage of the yacht.

VIRTUS XP
